

Transportation Projects

Franklin Street Bridge

PROJECT DESCRIPTION

This project was to remove the old sub-standard two-lane bridge over the Union Pacific Railroad and replace it with a new bridge capable of carrying four lanes of traffic. The project also included expanding the bridge of Town Creek to accommodate four lanes of traffic and the intersection of Bridge Street and Vine Street was reconstructed to improve traffic visibility.

STATUS REPORT/ ALTERNATE ROUTES

A contract for construction was awarded to Orval Hall Excavating, Ltd. on November 18, 2008 and construction started December 8, 2008. Demolition of the old bridge over the railroad took place in March. Construction of the new bridge was well underway the week of April 20th. The project was on schedule and was due to be complete in November 2009. The project was completed and opened to traffic August 4, 2009.




Franklin Street Bridge Projected Timeline



Projected Costs

Description	Budget	YTD 01/10
Survey/ Design/ Environmental	\$325,000	\$320,759
Right of Way	\$10,000	\$6,169
Construction	\$1,850,000	\$1,842,782
Construction Admin/ Testing	\$147,066	\$110,630

Cost Distribution

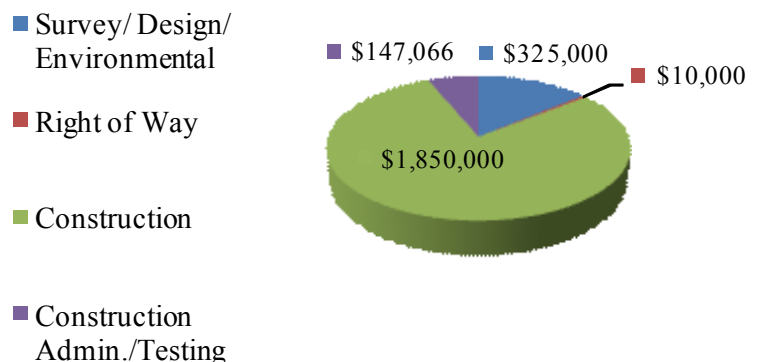

STAFF CONTACT INFORMATION:
 Terry Hughes, 817-598-4244
 Director of Transportation & Public Works
thughes@weatherfordtx.gov

